
SMART WEATHER

Agile Project Report | Scrum Master Summary

Project:	Smart Weather – Mobile & Web Forecasting Platform
Reporting Period:	Sprint 1 – Sprint 5 (10 weeks)
Framework:	Scrum (2-week sprint cadence)
Prepared By:	Scrum Master, Smart Weather Delivery Team
Tooling:	Jira Software (Scrum board, Backlog, Reports)
Report Date:	September 12, 2026

This report summarizes Agile/Scrum delivery progress for the Smart Weather project, tracked in Jira, including sprint performance, velocity and burndown metrics, backlog health, risks, and retrospective outcomes.

1. Project Overview

Smart Weather is a cross-platform (mobile + web) weather intelligence application that delivers real-time forecasts, hyperlocal alerts, and historical climate insights by combining public meteorological APIs with a network of low-cost IoT weather sensors. The product targets individual consumers as well as small agricultural and logistics operators who need reliable, location-specific weather data.

Core Objectives

- Deliver accurate, low-latency forecasts using a hybrid API + IoT sensor data pipeline.
- Provide severe-weather push notifications with under 60-second alert latency.
- Support offline caching for low-connectivity regions.
- Launch on iOS, Android, and a responsive web dashboard within two quarters.

Team & Roles

Role	Name / Group	Responsibility
Product Owner	A. Mehta	Backlog prioritization, stakeholder liaison
Scrum Master	R. Kapoor	Facilitation, impediment removal, Jira hygiene
Frontend Team	3 engineers	Mobile (iOS/Android) & web dashboard UI
Backend Team	3 engineers	APIs, data pipeline, forecasting service
IoT/Hardware Team	2 engineers	Sensor firmware, edge data ingestion
QA	2 engineers	Test automation, release validation

2. Agile / Scrum Process Summary

The team follows Scrum with two-week sprints, managed end-to-end in Jira Software. Epics are tracked at the Jira project level, broken into user stories and sub-tasks, estimated in story points, and pulled into sprint backlogs during Sprint Planning.

Ceremony	Cadence	Purpose
Sprint Planning	Start of each sprint	Select and estimate backlog items for the sprint
Daily Standup	Daily, 15 min	Sync on progress, blockers, and next steps
Backlog Refinement	Weekly	Groom, split, and re-estimate upcoming stories
Sprint Review	End of each sprint	Demo completed work to Product Owner & stakeholders
Sprint Retrospective	End of each sprint	Reflect on process and agree on improvement actions


3. Sprint-by-Sprint Summary

Sprint	Goal	Committed	Completed	Status
Sprint 1 (Wk 1-2)	Stand up backend skeleton & integrate primary weather API	28	22	Completed
Sprint 2 (Wk 3-4)	Build forecast UI screens & onboarding flow	30	27	Completed
Sprint 3 (Wk 5-6)	Integrate IoT sensor data ingestion pipeline	32	30	Completed
Sprint 4 (Wk 7-8)	Implement push alerts & offline caching	34	31	Completed
Sprint 5 (Wk 9-10)	Web dashboard MVP & hardening for beta release	32	30	In Progress

Key Jira epics tracked across sprints: **SW-101 Forecast Engine**, **SW-142 IoT Sensor Ingestion**, **SW-178 Alerts & Notifications**, **SW-205 Offline Mode**, and **SW-233 Web Dashboard**.


4. Jira Metrics Dashboard

4.1 Sprint Velocity

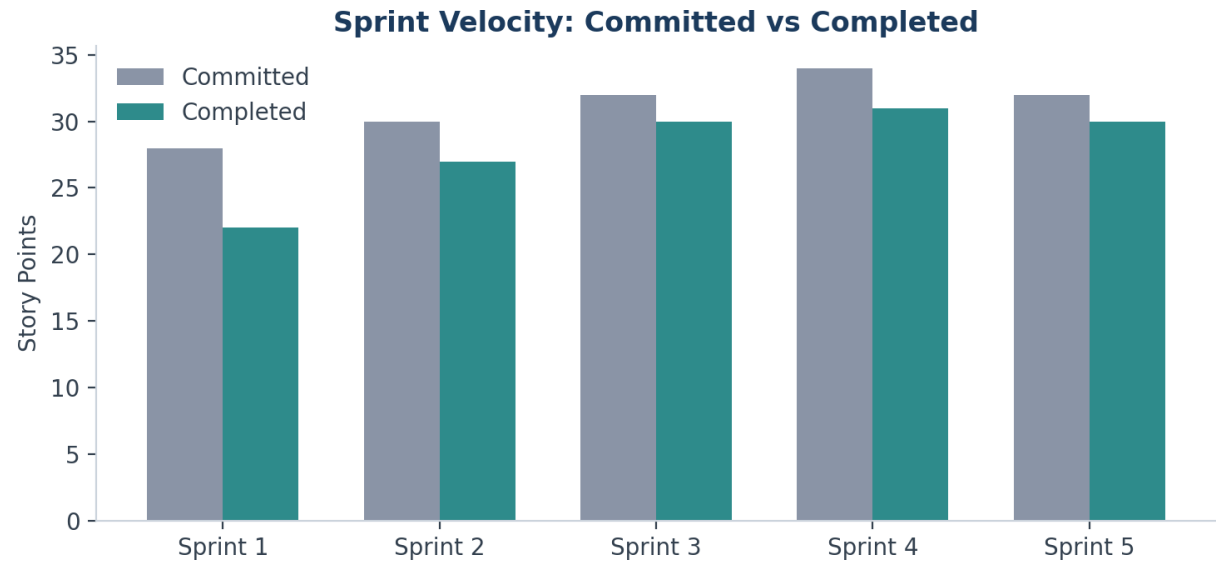

Average velocity across five sprints is approximately **28 story points**, with completion rate stabilizing around 92-95% of committed points from Sprint 3 onward, indicating improved estimation accuracy as the team matured.


4.2 Current Sprint Burndown (Sprint 5)

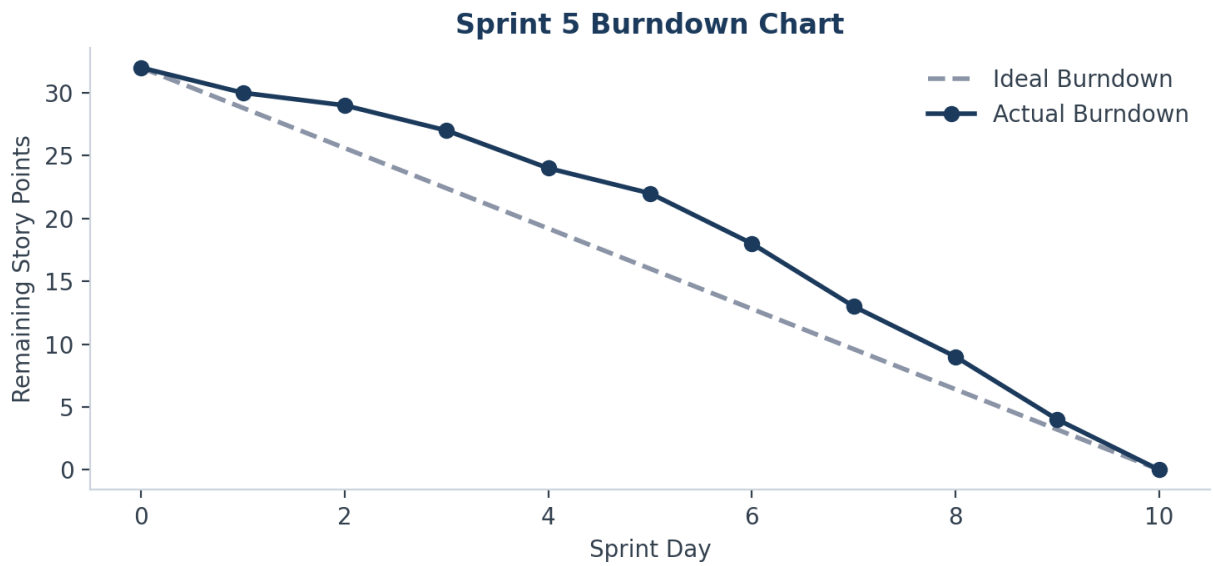

The team tracked slightly behind the ideal line mid-sprint due to a third-party weather API rate-limit issue (see Risks & Issues), but recovered pace in the final three days.

4.3 Backlog Health

Backlog Breakdown by Status (Total Issues)

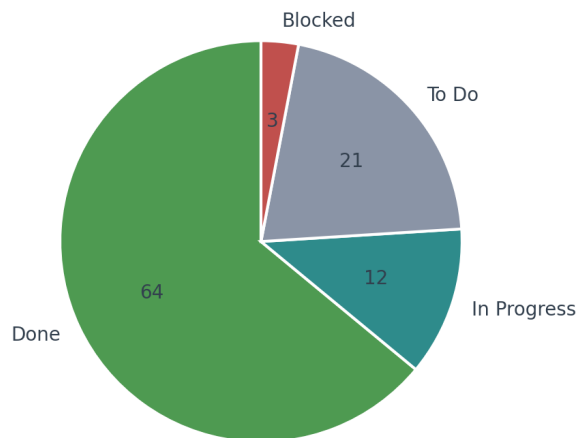

Of 100 tracked issues in the Smart Weather Jira project, 64 are Done, 12 In Progress, 21 remain in To Do, and 3 are currently Blocked pending external dependencies.

5. Risks & Issues Log

ID	Risk / Issue	Impact	Mitigation	Status
R-01	Third-party weather API rate limits during peak load	High	Add caching layer & negotiate higher rate tier	Mitigating
R-02	IoT sensor firmware battery drain in field tests	Medium	Optimize polling interval; firmware patch in Sprint 6	Open

R-03	Delayed app store review for iOS beta build	Medium	Submit build 5 days ahead of planned release	Monitoring
R-04	Cross-team dependency between Alerts and Notification service	Low	Weekly sync between Backend and Frontend leads	Resolved

6. Retrospective Highlights (Sprint 4 & 5)

What Went Well

- Cross-functional pairing between Backend and IoT teams reduced integration bugs.
- Story point estimation accuracy improved after adopting Planning Poker.
- Zero critical production incidents during the reporting period.

What Didn't Go Well

- Ambiguous acceptance criteria on two stories caused mid-sprint rework.
- Third-party API rate limiting was not identified as a risk early enough.

Action Items

- Add a Definition of Ready checklist item for acceptance criteria review before sprint planning.
- Create a dedicated Jira risk-tracking board column reviewed at every backlog refinement.
- Schedule a spike in Sprint 6 to evaluate a secondary weather data provider.

7. Upcoming Sprint Plan & Next Steps

Sprint 6 (Weeks 11-12) will focus on closing out the Web Dashboard MVP, resolving open risks R-01 and R-02, and preparing the release candidate for closed beta with approximately 200 external users. The Product Owner will finalize the beta feedback intake process in Jira via a dedicated 'Beta Feedback' issue type.

Focus Area	Target Sprint	Owner
Web Dashboard MVP completion	Sprint 6	Frontend Team
Resolve API rate-limit risk (R-01)	Sprint 6	Backend Team
Sensor firmware battery fix (R-02)	Sprint 6	IoT/Hardware Team
Closed beta release & feedback loop setup	Sprint 7	Product Owner
